

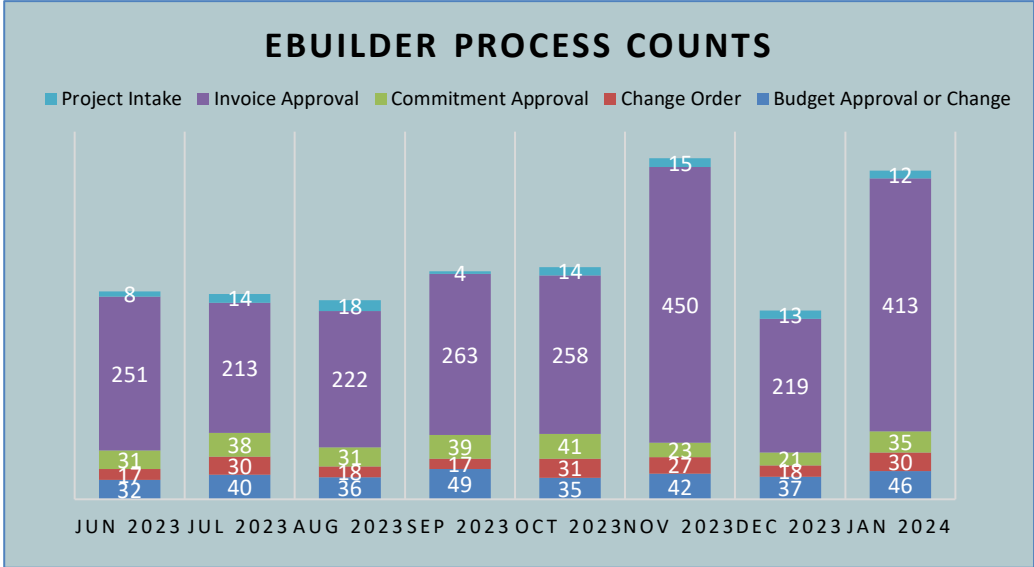
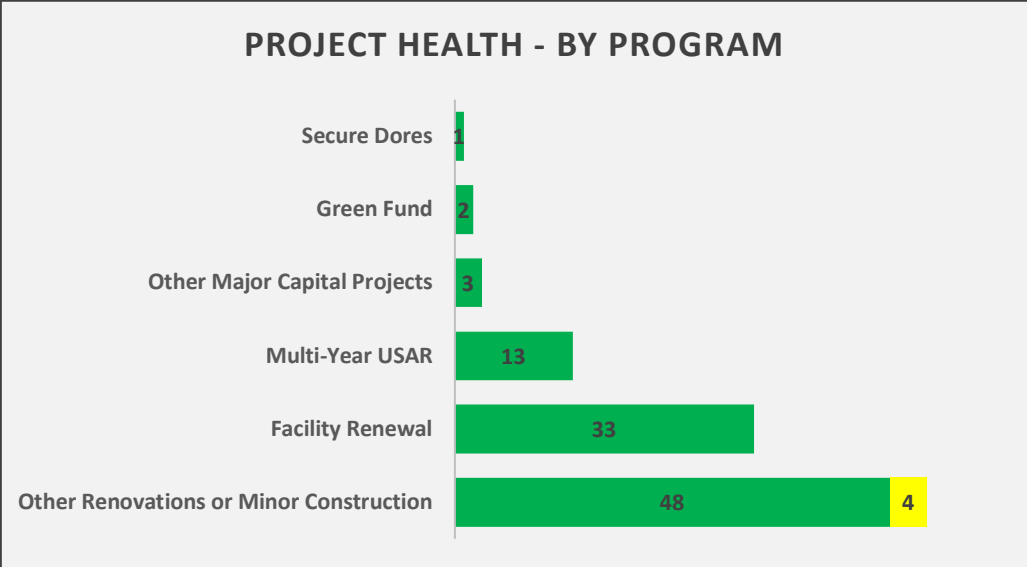
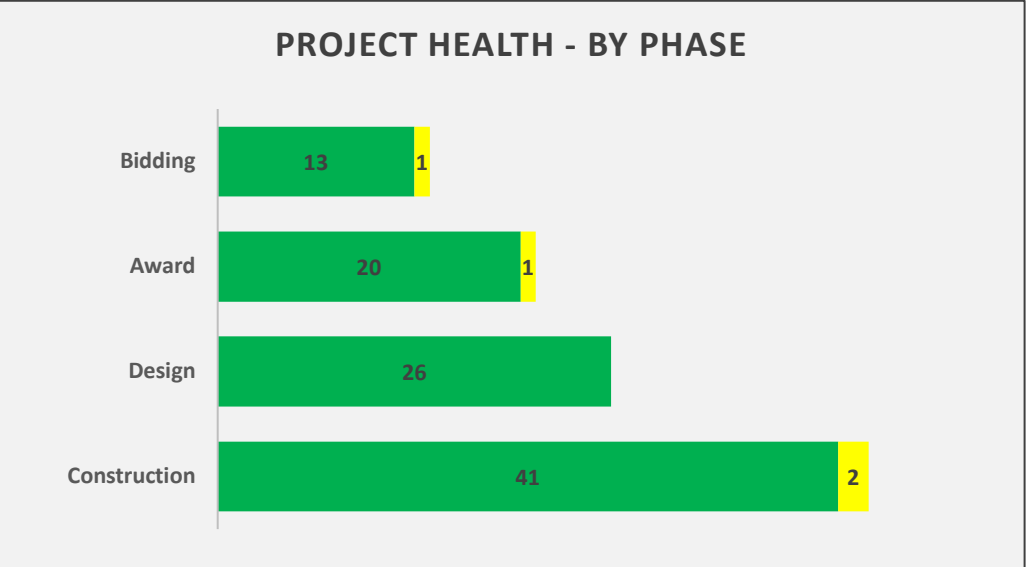
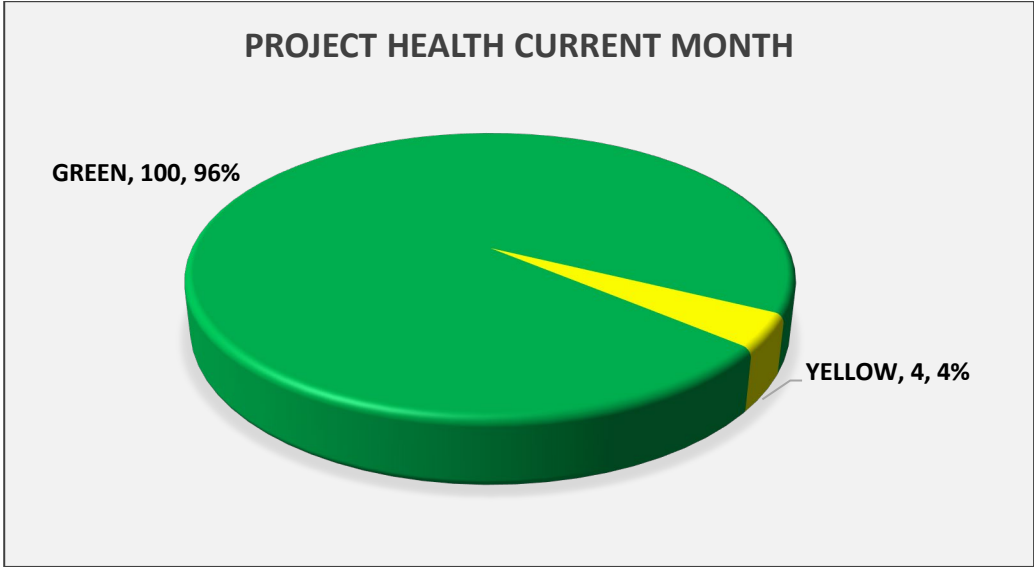


Active Project Health - JANUARY 2024

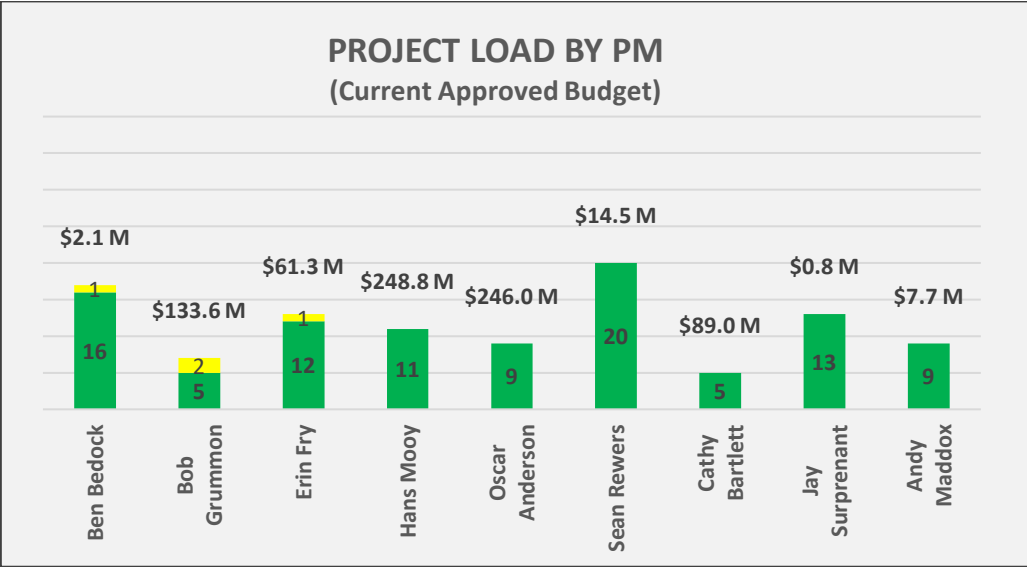

PROJECTS	RATING	COMMENTS
Football Stadium - Pressbox Roof Replacement	YELLOW	once approval to proceed is given the schedule will be reevaluated to ensure completion prior to the beginning of the season.
Football Stadium - Television Booth Renovation	YELLOW	Need athletics approval for additional funding, once received we will evaluate whether work can be completed prior to start of season.
Chancellor's Residence	YELLOW	We brought Landon Development on at the beginning of the project, but let them go. We re-bid the project to several high-end residential firms who declined to respond. We have decided to work with campus partner Beech construction and require that they use a quality millworker approved by Dryden. The construction and furniture should coincide in late April/ Early May. The resident would like to move in sooner, so we are working on ways to accommodate that, such as temp furniture and making the laundry room renovation a Phase 2.
Sarratt Student Center - West Wing Third Floor Renovation	YELLOW	Project is pending the hiring of an engineer to weigh in on design. Working to determine impact to schedule.
		Green - Project is on schedule and on budget.
		Yellow - Potential impact to schedule and/or budget. See health comment for more details.
		Red - Impact to schedule and/or budget. See health comment for more details.

NOTE: All comments are confidential.

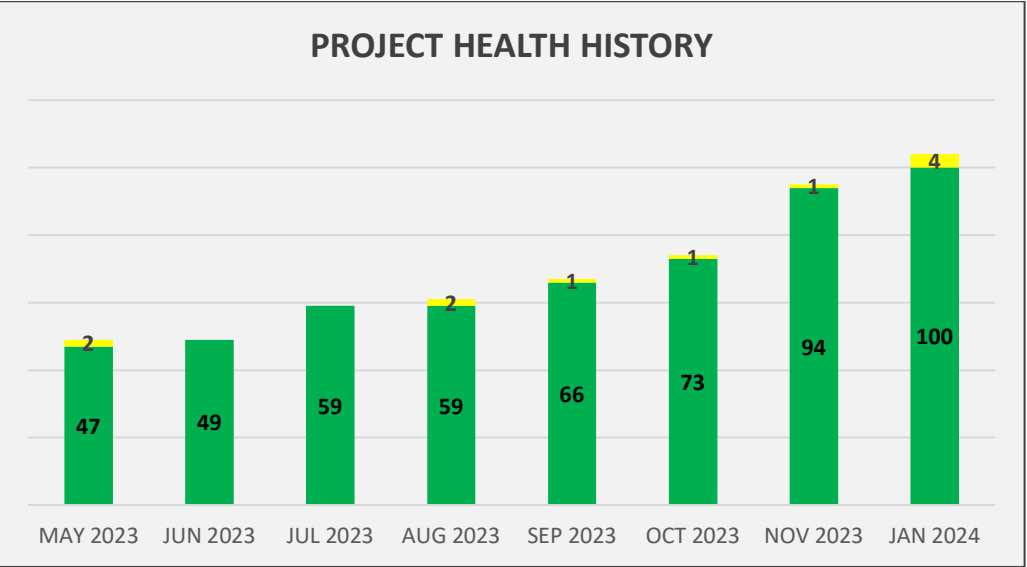
