


ID	Task Name	Duration	Start	Finish	Resource Names	r 1							
						11/8	11/15	November 21		December 11			12
						11/22	11/29	12/6	12/13	12/20	12/27		
1	Design	75 days	Mon 11/16/15	Fri 2/26/16									
2	Silicone Halo	70 days	Mon 11/16/15	Fri 2/19/16	Team								
3	Module	70 days	Mon 11/16/15	Fri 2/19/16	Team								
4	Circuit	75 days	Mon 11/16/15	Fri 2/26/16	LP								
5	Battery Decision	75 days	Mon 11/16/15	Fri 2/26/16	AZS								
6	IRB Application	65 days	Mon 11/23/15	Fri 2/19/16									
7	Device Protocol	63 days	Mon 11/23/15	Wed 2/17/16	ES,BF								
8	Consent Form	63 days	Mon 11/23/15	Wed 2/17/16	ES,BF								
9	DISCOVER-e Online	63 days	Mon	Wed 2/17/16	JM								
10	Submission	3 days	Wed 2/17/16	Fri 2/19/16	JM								
11	Prototype Construction	45 days	Mon 1/18/16	Fri 3/18/16									
12	Silicone Halo	16 days	Mon 1/18/16	Mon 2/8/16	SS								
13	Module	40 days	Mon 1/25/16	Fri 3/18/16	AZS,LP,SS								
14	Circuit	45 days	Mon 1/18/16	Fri 3/18/16	AZS,LP								
15	Battery	35 days	Mon 2/1/16	Fri 3/18/16									
16	Ordering	4 days	Wed 2/24/16	Mon 2/29/16	LP								
17	Testing	5 days	Mon 2/29/16	Fri 3/4/16	AZS,LP								
18	Feasibility Study	23 days	Mon 3/21/16	Wed 4/20/16									
19	IRB Approval	1 day	Fri 3/18/16	Fri 3/18/16									
20	Study / Trials	23 days	Mon 3/21/16	Wed 4/20/16	Team,Hicks								
21	Design Day	1 day	Mon 4/25/16	Mon 4/25/16									



Project: LumaSil
Date: Wed 2/24/16

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

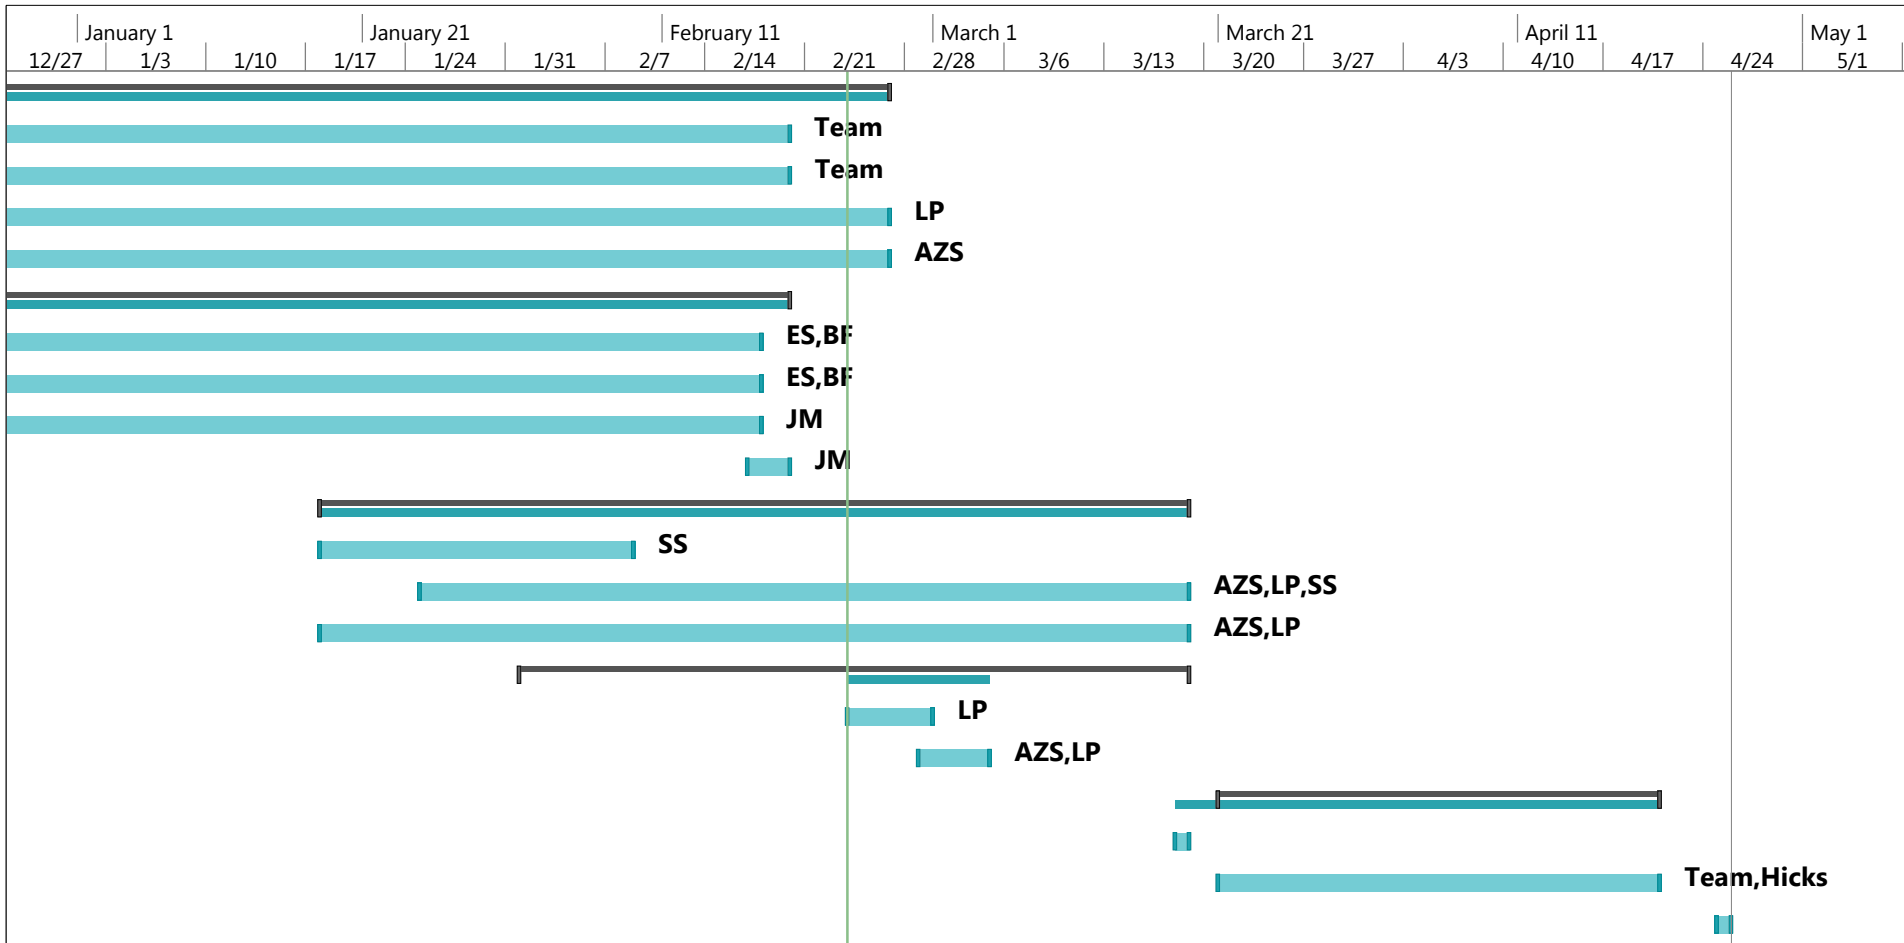

Project: LumaSil
Date: Wed 2/24/16

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			
