































ID	 Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Sep 25, '16					
								S	T	T	S		
1		<b>Summary #1</b>	<b>32 days</b>	<b>Thu 9/29/16</b>	<b>Fri 11/11/16</b>								
2		Read and Review Material from Michael	7 days	Thu 9/29/16	Fri 10/7/16								
3		Document Preliminary Design Ideas	3 days	Mon 10/10/16	Wed 10/12/16	2							
4		Meet with Michael and/or Dr. Migas	1 day	Thu 10/13/16	Thu 10/13/16	3							
5		Draw up sketches from preliminary ideas	3 days	Fri 10/14/16	Tue 10/18/16								
6		Re-evaluate design, identify flaws and shortcomings	6 days	Wed 10/19/16	Wed 10/26/16								
7		Meet with Michael and/or Dr. Migas	1 day	Sun 10/23/16	Sun 10/23/16								
8		Begin work on BMEidea proposal application first draft	3 days	Tue 10/25/16	Thu 10/27/16								
9		Submit BMEidea proposal first draft	1 day	Thu 10/27/16	Thu 10/27/16								
10		View shunt placement surgery	1 day	TBD									


Project: Simple Project Plan  
Date: Mon 10/24/16

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Sep 25, '16				Oc
								S	T	T	S	
11		Integrate new knowledge of neuro-physiology into design	5 days	Fri 10/28/16	Thu 11/3/16							
12		Meet with Michael and/or Dr. Migas	1 day	Thu 11/3/16	Thu 11/3/16							
13		Draw up sketches from newest iteration of ideas	3 days	Fri 11/4/16	Tue 11/8/16							
14		Sketch design in Creo	3 days	Wed 11/9/16	Fri 11/11/16							


Project: Simple Project Plan  
Date: Mon 10/24/16

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

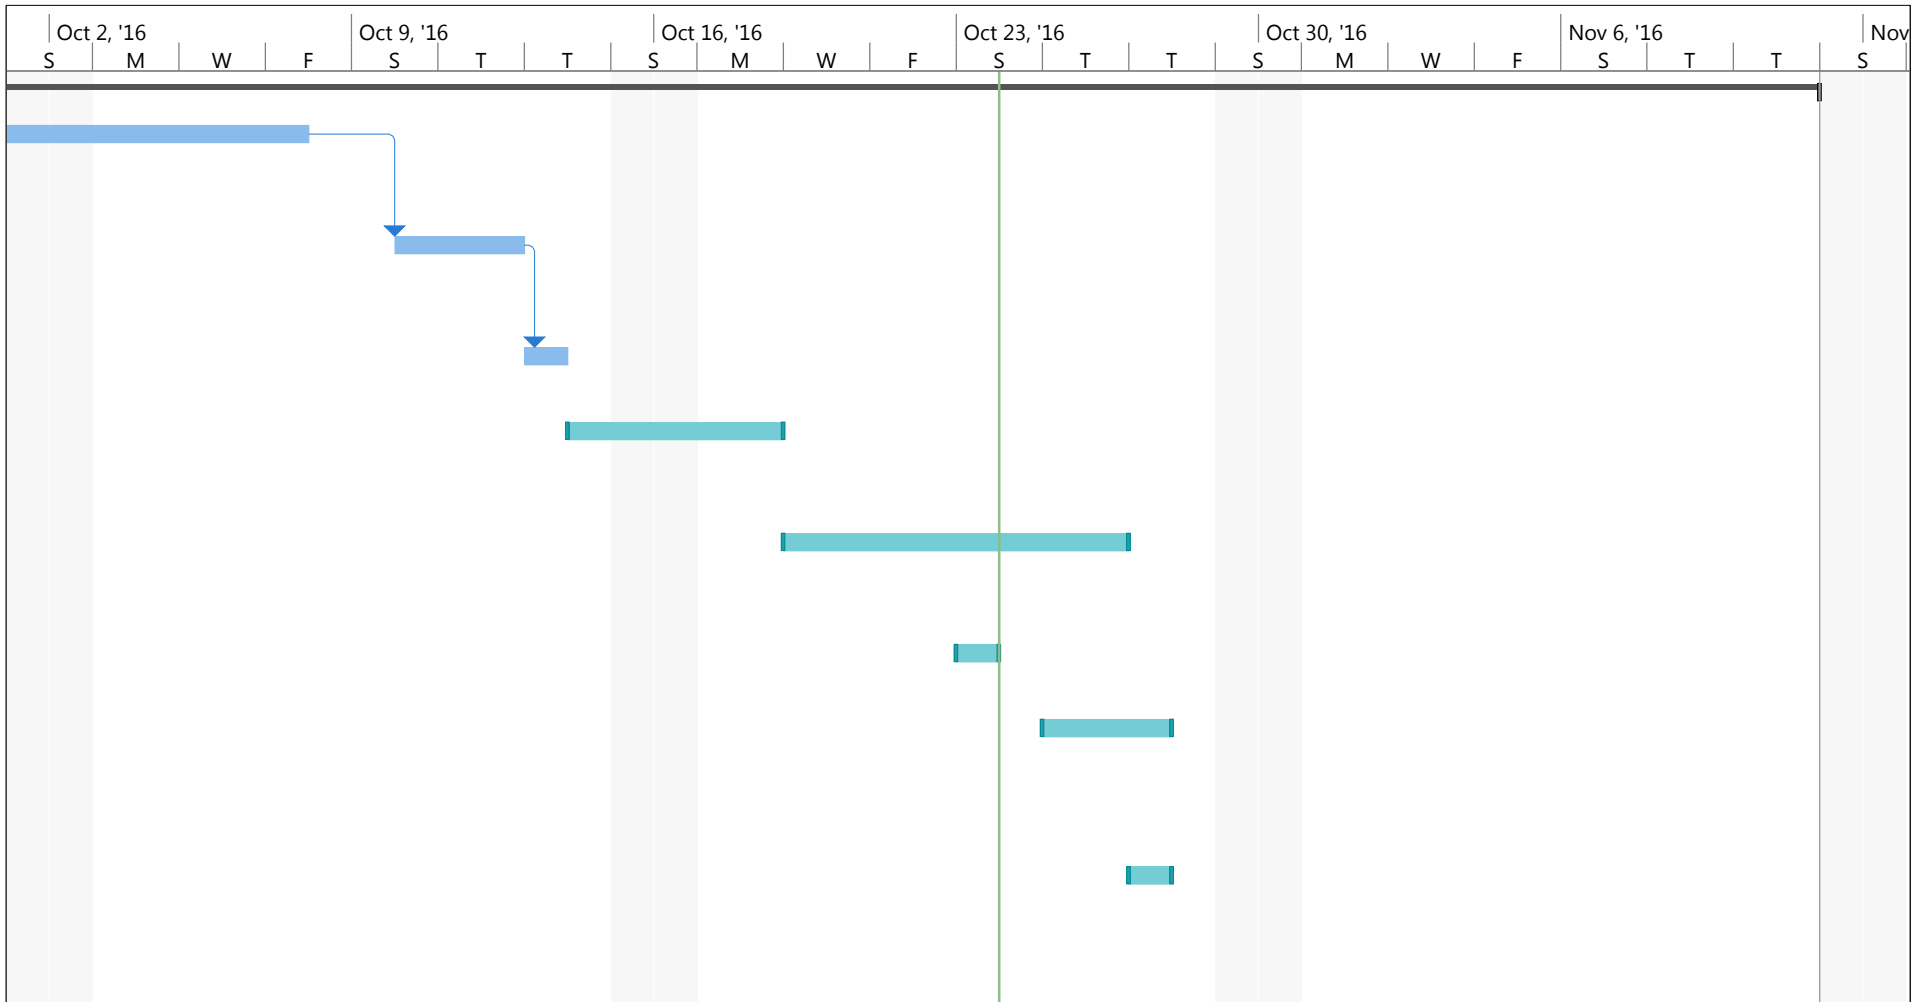

Project: Simple Project Plan  
Date: Mon 10/24/16

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

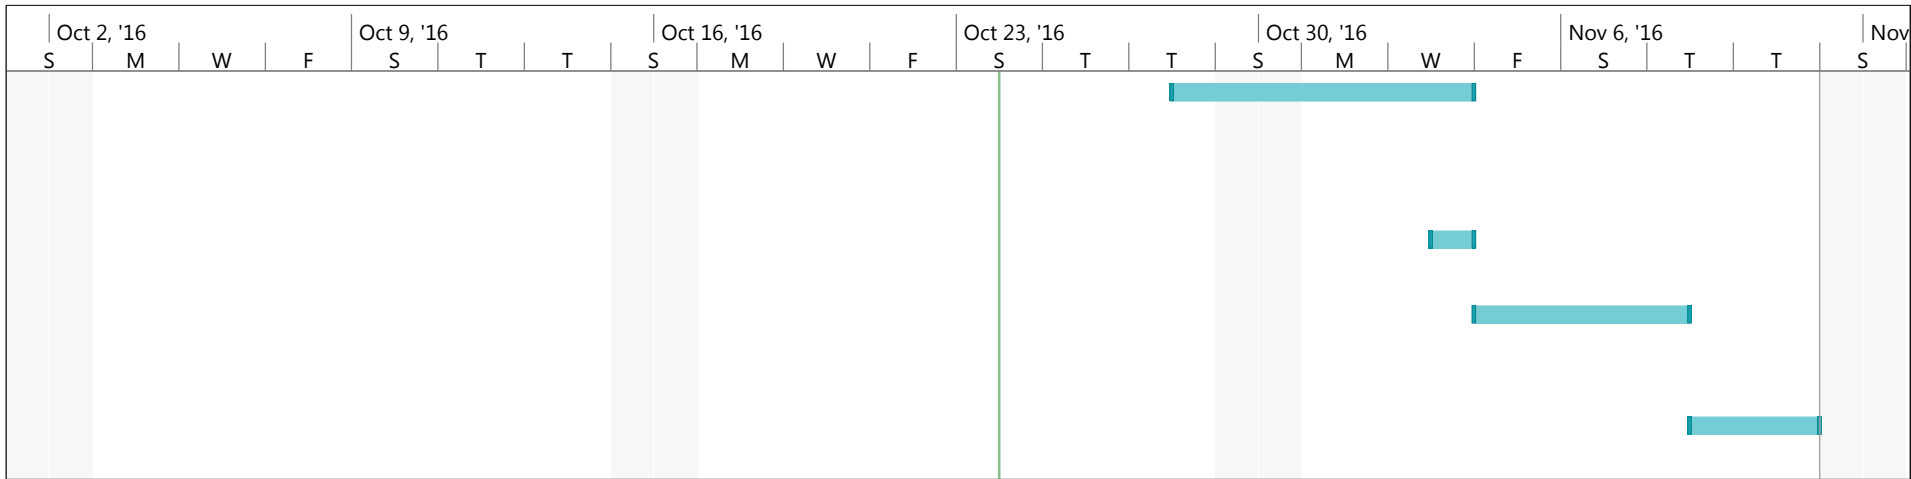

Project: Simple Project Plan  
Date: Mon 10/24/16

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			
